Redesigning the Healthy City Dashboard

Mode Share Indicator Page | PM & Dev Retrospective

Presented by Hilal (Dev Lead)

Project Overview

The Goal

Redesign the Mode Share indicator page of Vancouver's Healthy City Dashboard. The objective was to transform complex transportation data into accessible, interactive insights.

My Role: Dev Lead

- **Development:** Built the front-end prototype, using HTML, CSS JavaScript and handled JSON data integration, and built interactive Chart.js visualizations.
- **Project Management:** Partnered with Char to manage Jira backlogs, sprint planning, and risk mitigation strategies.

As mentioned in: FDIT 2110 Assignment 1.1

PM Contribution & Impact

Strict Schedule

Managed a strict weekly schedule ensuring zero late tasks using weekly sprints.

100% Completion

From Weeks 6-9, completed 15 tasks with 100% completion rate. JSON functional code finished by Week 9.

Zero-Cost Model

Operated efficiently using open-source tools (Figma, VS Code, Chart.js) to maximize value.

As mentioned in: FDIT 2110 Assignment 1.5

Applying PM Principles

MoSCoW Prioritization

- **Must Have:** Interactive mode share chart, year/region filtering.
- **Won't Have:** Live data updates from City API.
- **Impact:** Prioritizing JSON charts over complex GeoJSON maps prevented delays.

Velocity & Sprint Planning

- **Planning:** Deliverables broken down by week (Week 7 Hi-Fi, Week 8 Functional).
- **Velocity:** Maintained steady output (5-6 tasks/week).
- **Outcome:** Discipline allowed us to finish functional code early for QA.

As mentioned in: FDIT 2110 Assignment 1.2

S.T.A.R. Example: Technical Risk



Situation

Faced a 2-day Figma outage and GeoJSON risks threatening Week 8 deadline.



Task

Ensure Functional Code milestone was delivered on time.



Action

Utilized outage for code self-testing; facilitated peer testing to catch bugs early.



Result

Completed JSON functional code fully in Week 8 with zero errors.

Challenges & Solutions

Key Challenges

- Different early design ideas, alignment needed
- Scope confusion in Week 4
- Real data not matching chart mockups
- Integration took longer than planned
- Many small spacing + microcopy issues in A04
- Debugging real chart behaviour (labels, scale, responsiveness)

How We Solved These

- A/B tested wireframes to choose best direction
- Met with instructor to re-scope project
- Held frequent check-ins to align design & dev
- Conducted bug testing + QA to uncover inconsistencies
- Built issue log to prioritize final fixes
- Refined spacing, labels, and visual hierarchy in A04

Outcome

A polished final dashboard that matched design goals and functioned smoothly.

Process Timeline



Weeks 2-5

Define
Research & Lo-Fi
Validated
Wireframes

Weeks 6-7

Design
Hi-Fi Prototype
Design System
Sync


Weeks 8-9

Develop
JSON Integration
Functional Code
(Hilal)

Weeks 10-12

Deploy
Final QA &
Polish
Live Demo Prep


User Persona

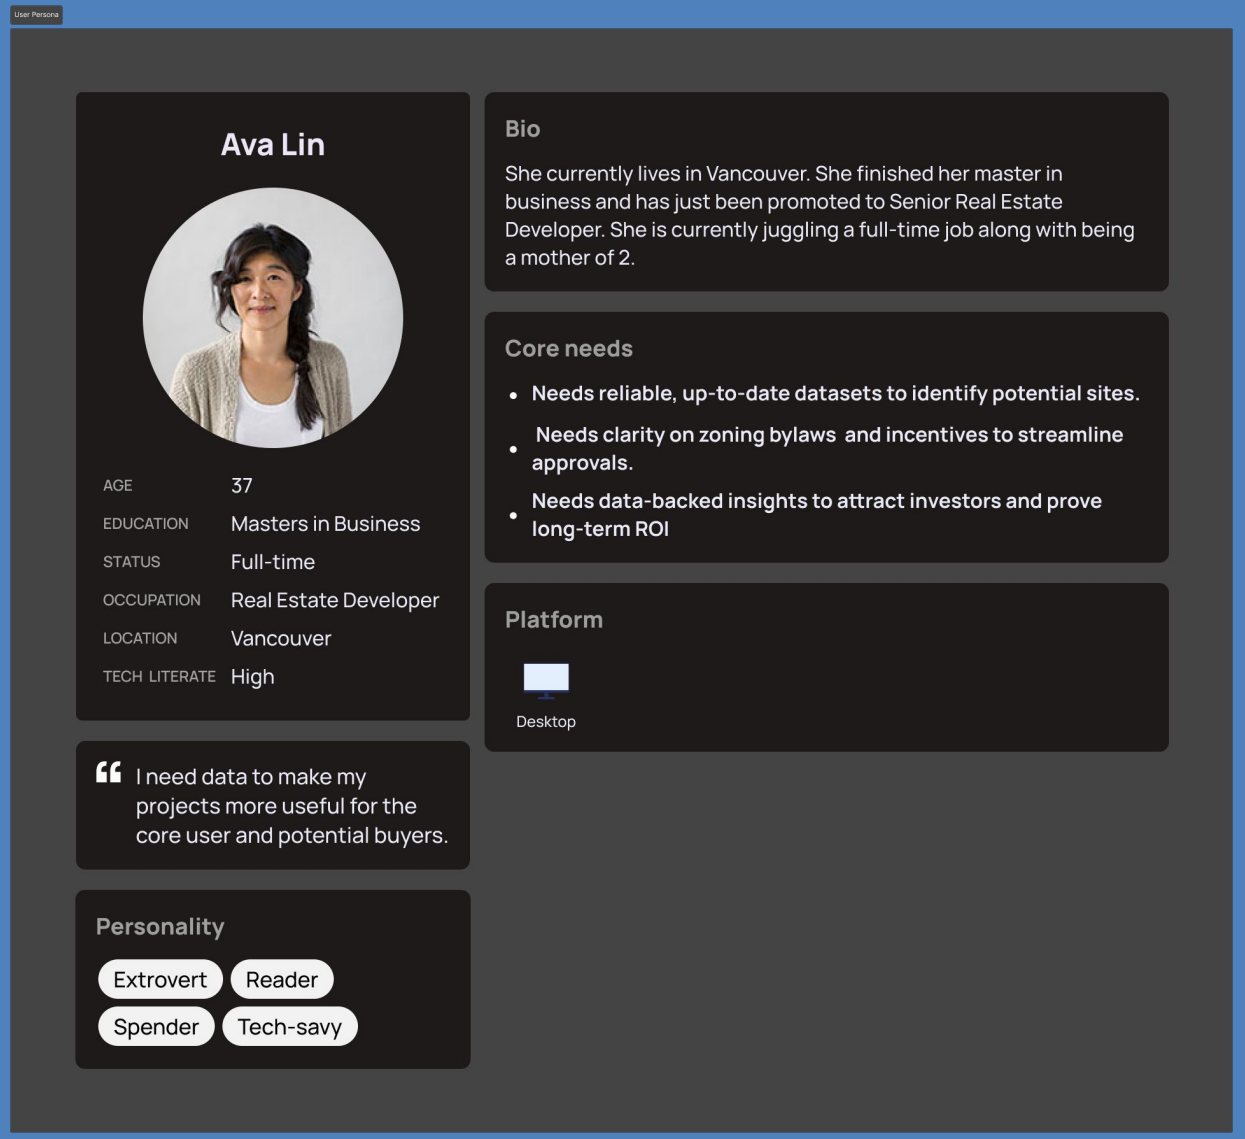


The User Persona was a critical tool used early in the project to define our target audience,
the non-technical city stakeholder or engaged citizen who needed accessible data.

By focusing on their needs and limitations, the persona directly informed the design choices for the Mode Share indicator page, ensuring we successfully transformed complex, raw transportation data into a user-friendly, interactive format.


Wireframe stage.

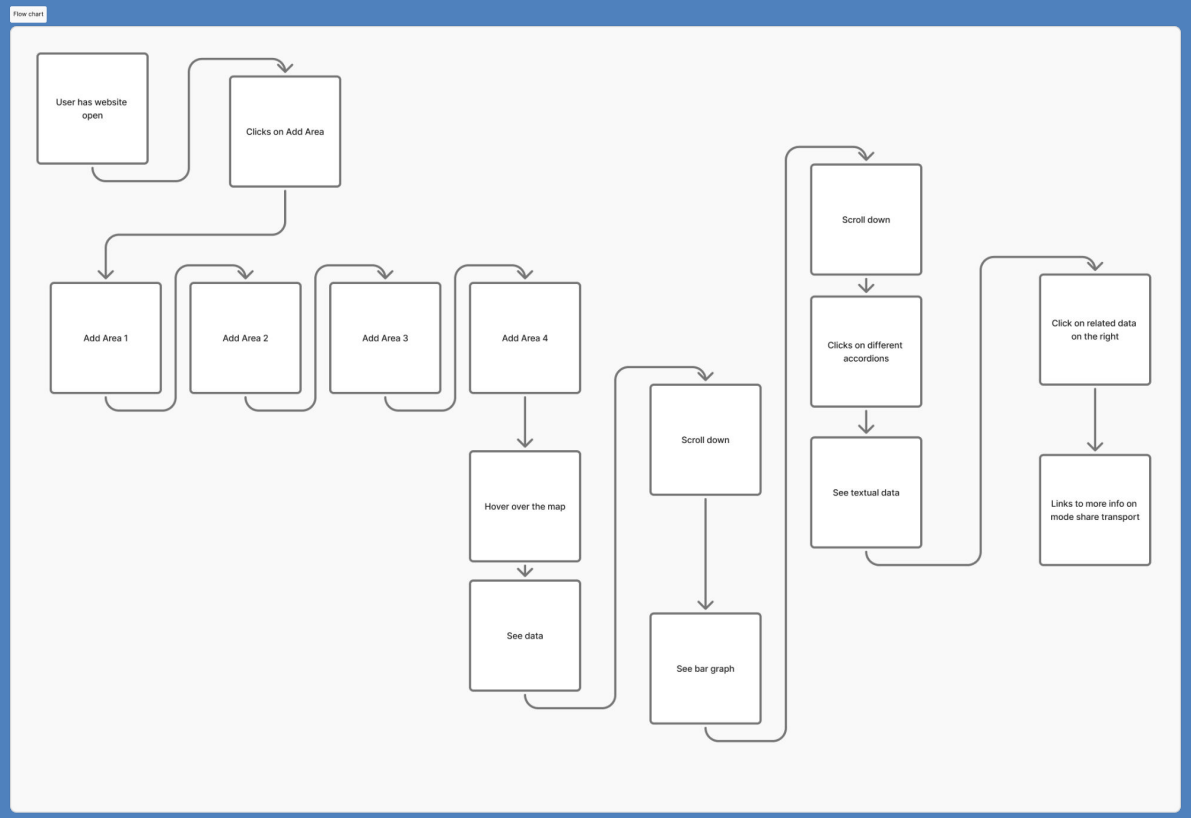


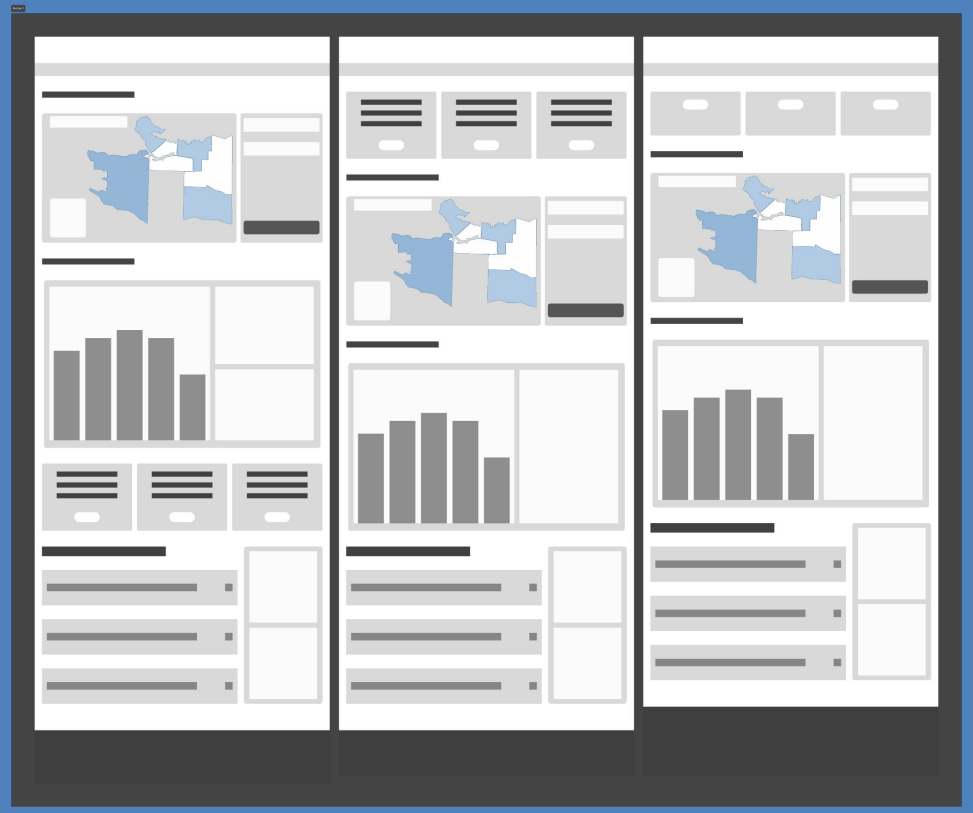


The wireframe stage, occurring during Weeks 2-5, focused on the initial **Define, Research & Lo-Fi** steps of the project. We created and validated low-fidelity wireframes to establish the core layout and information architecture for the Mode Share indicator page. This foundational work ensured early alignment on the user experience before proceeding to the Hi-Fi design stage.

Hi-fi design Stage

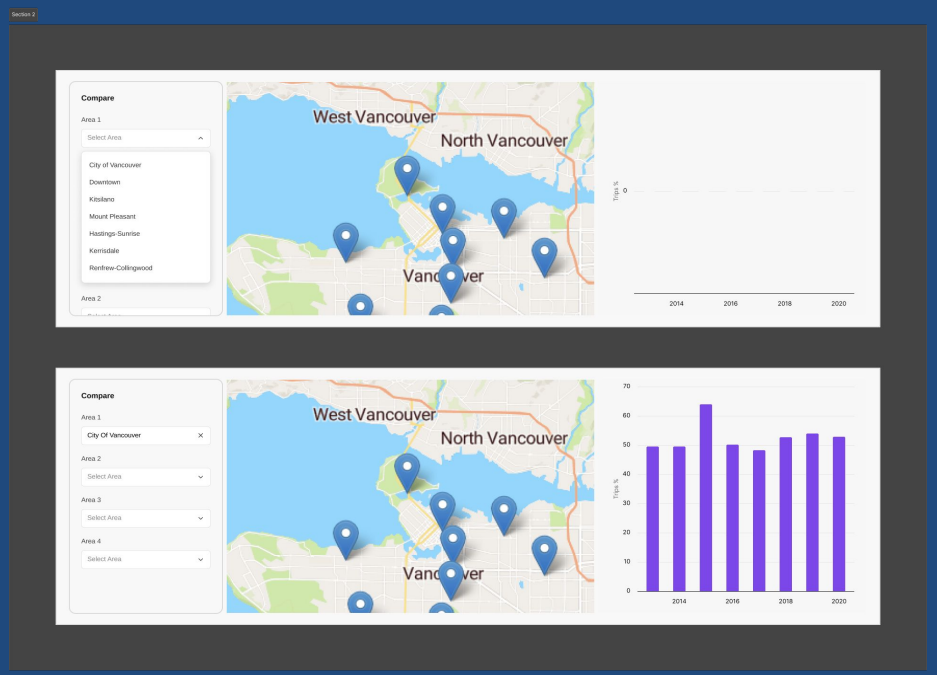

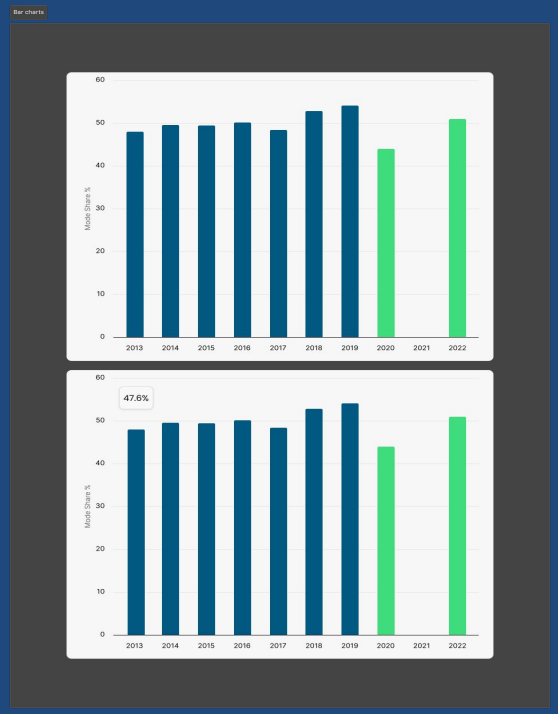


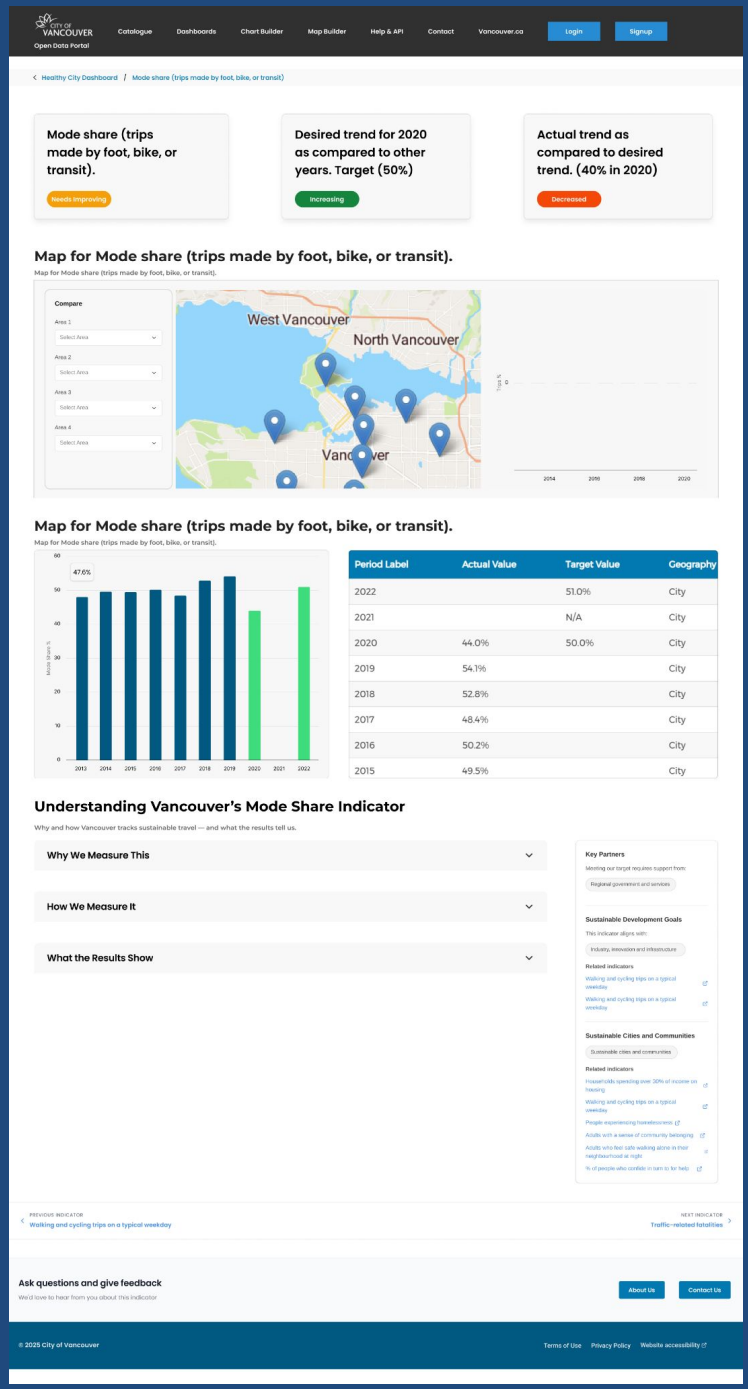

The Hi-fi design Stage, taking place during **Weeks 6-7** as per our timeline, involved transforming the validated low-fidelity wireframes into a complete, visually refined prototype. This phase focused on applying the Design System to ensure brand cohesion, selecting final color palettes and typography, and integrating detailed microcopy. The outcome was a high-fidelity mock-up that served as the definitive blueprint for the subsequent development and JSON integration phase.


Development Stage




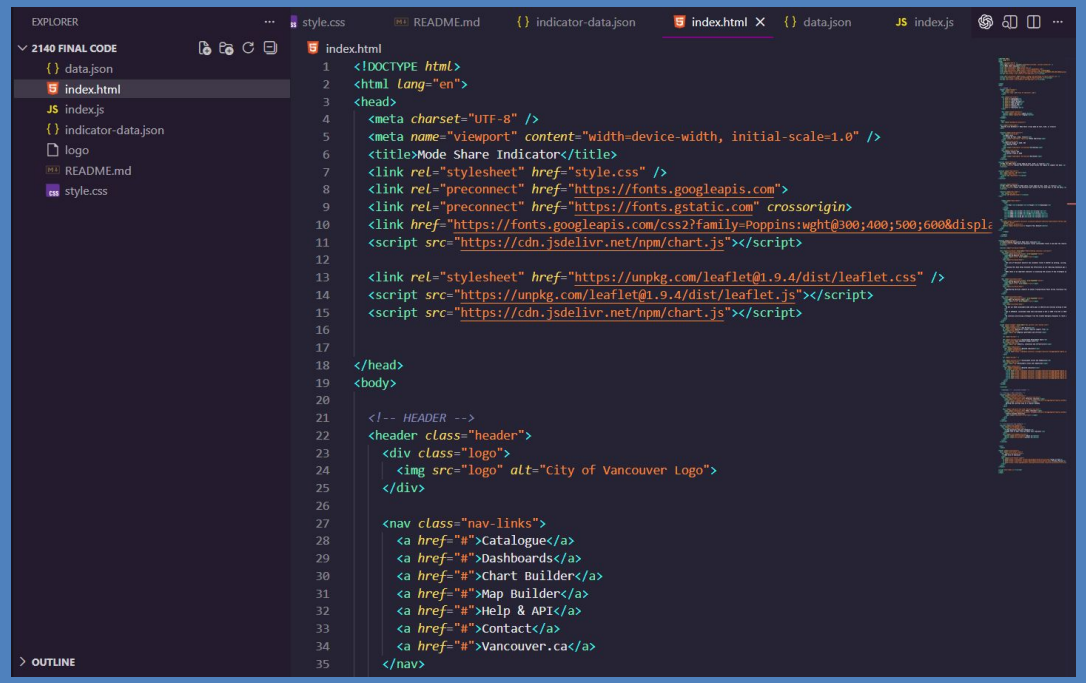

The Development Stage, spanning **Weeks 8-9** of the project timeline, was focused on **JSON Integration** and delivering the **Functional Code**. As the Dev Lead, I built the front-end prototype using HTML, CSS, and JavaScript, successfully integrating JSON data to create interactive Chart.js visualizations. Despite facing technical risks, we maintained a strict schedule and finished the functional code with a 100% completion rate by Week 9, allowing for early QA.

Deployment Stage

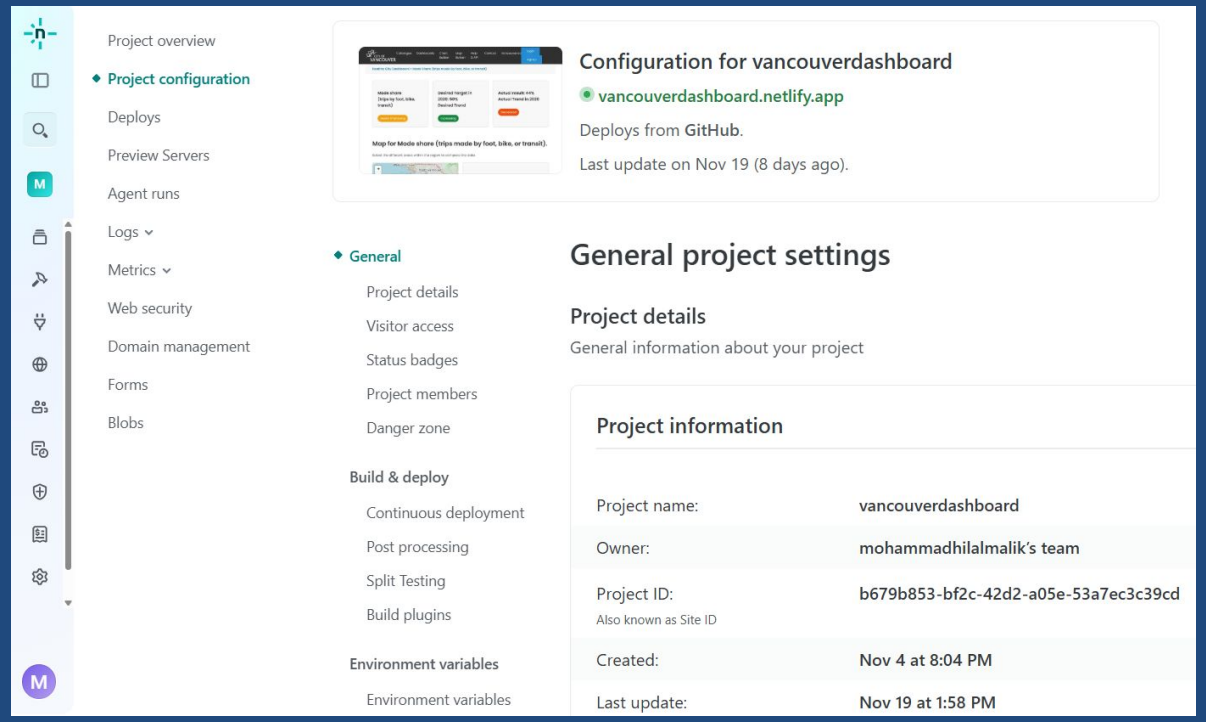

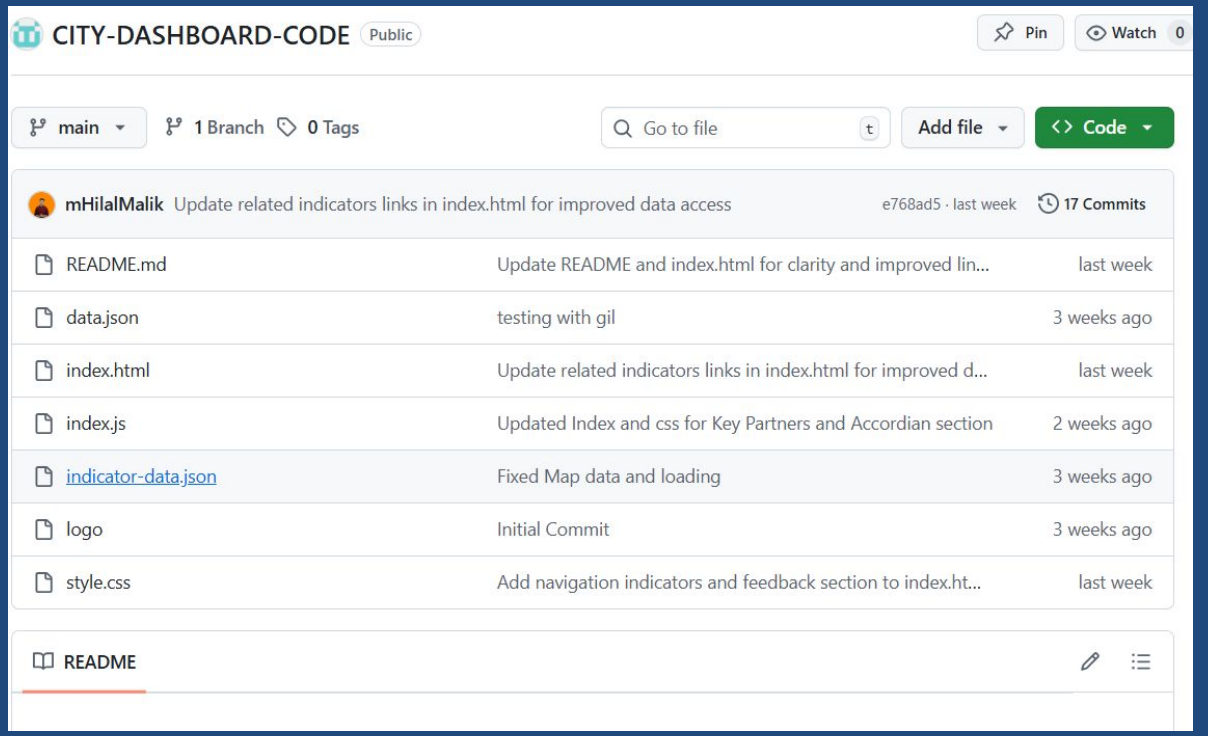

After finishing the functional code in Week 9, the project transitioned to the deployment pipeline. The code was uploaded to **GitHub** for version control, then linked to **Vercel**. This setup enabled continuous deployment, automatically building and hosting the dashboard. For Weeks 10–12, this process facilitated final QA and polish, such as accessibility checks and design system integration, ensuring a reliable, up-to-date environment for the live demo.

Reflections: Impact & Outcomes



Unified Product

Design System integration made the dashboard cohesive.



Accessibility

Achieved Accessibility standards (Like contrast, focus states and keyboard navigation).



Responsiveness

Dashboard adapts smoothly to different desktop widths.



Reliability

JSON-based approach ensured stable demo data.

As mentioned in: FDIT 2110 Assignment 1.6

What Would I Do Differently?



Lock Core Features Earlier

Integration took longer than expected. I would freeze features one week earlier to focus on "the last 10%" polish.



More User Testing at various Stages

I would test designs and code at various stages (e.g., wireframes) to ensure we meet the project scope efficiently, rather than just testing the final build.

Questions?

Thank you for listening.

Hilal & Char | FDIT 2110
